5 HOLLONDS STREET WORKS

KERB WORKS TIMING: EARLY TO MID-MARCH 2016.

LANDSCAPE WORKS TIMING: LATE MARCH 2016. KIEWA CRESCENT WORKS

KERB WORKS TIMING: EARLY TO LATE FEBRUARY 2016.

LANDSCAPE WORKS TIMING: EARLY MARCH 2016.

> 1 PARK STREET WORKS

> > KERB WORKS TIMING: DECEMBER 2015, commencing Monday 30 November and finishing by 24 December.

LANDSCAPE WORKS TIMING: JANUARY 2016, commencing Monday 11 January and finishing

ASPHALTING WORKS TIMING (PARK ST, KIEWA CRES, LAKESIDE AVE & HOLLONDS ST): MID TO LATE MARCH 2016.

## MOUNT BEAUTY PROGRESSING PLACE PROJECT PROPOSED TOWN CENTRE WORKS TIMING

20 November 2015



The Mount Beauty Progressing Place project works are about to commence in the Town Centre.

The proposed timing of the kerb, landscape and asphalting works are indicated on this plan.


The attached plans illustrate the planned changes to kerbs and parking layouts.


Further information can be found on the Alpine Shire Council website under the 'Major Projects' tab.

If you have any questions about the works or the planned changes, please contact Francine Stacey on 5755 0567 or via email francines@alpineshire.vic.gov.au.





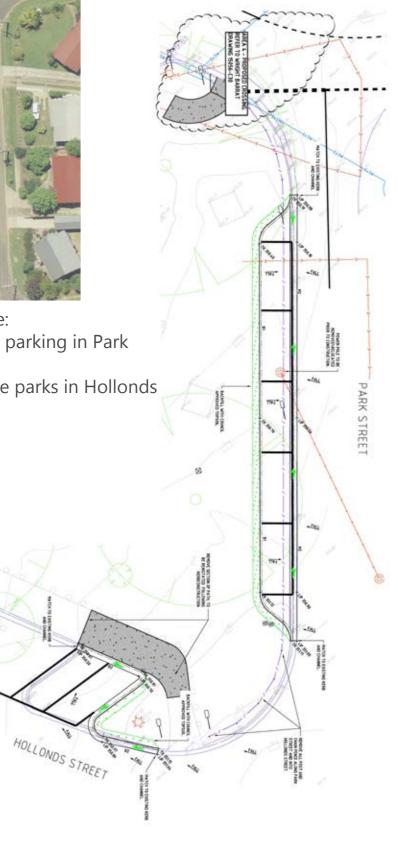


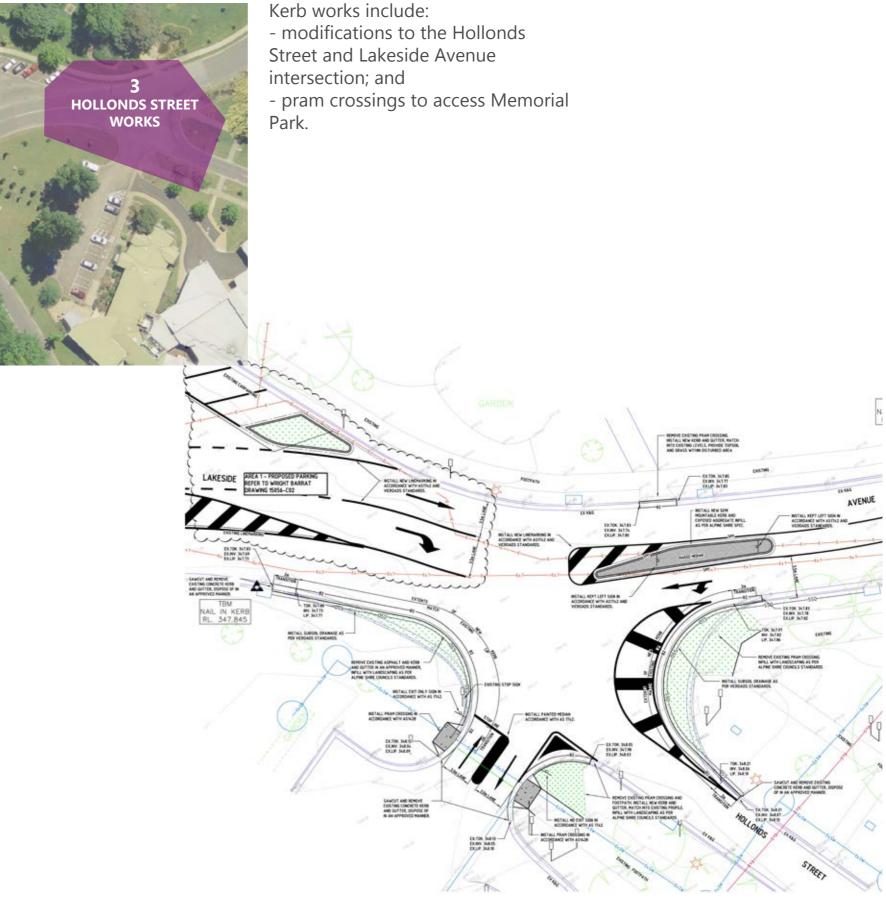

## MOUNT BEAUTY PROGRESSING PLACE PROJECT **PROPOSED TOWN CENTRE KERB WORKS**


20 November 2015



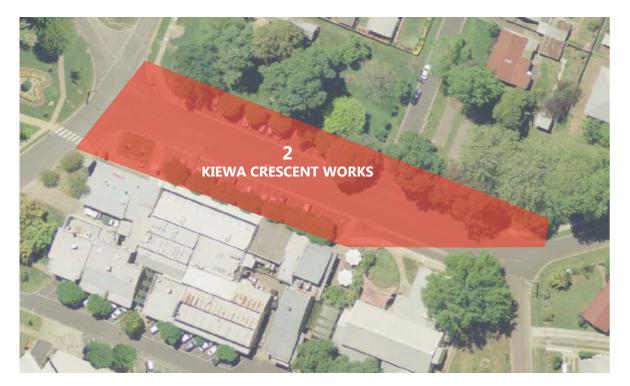

Kerb works include:

- changing right angle parking to angle parking;
- pedestrian refuge at western end
- of Kiewa Crescent; and
- extension of footpath from Park Street to Beauty Avenue.

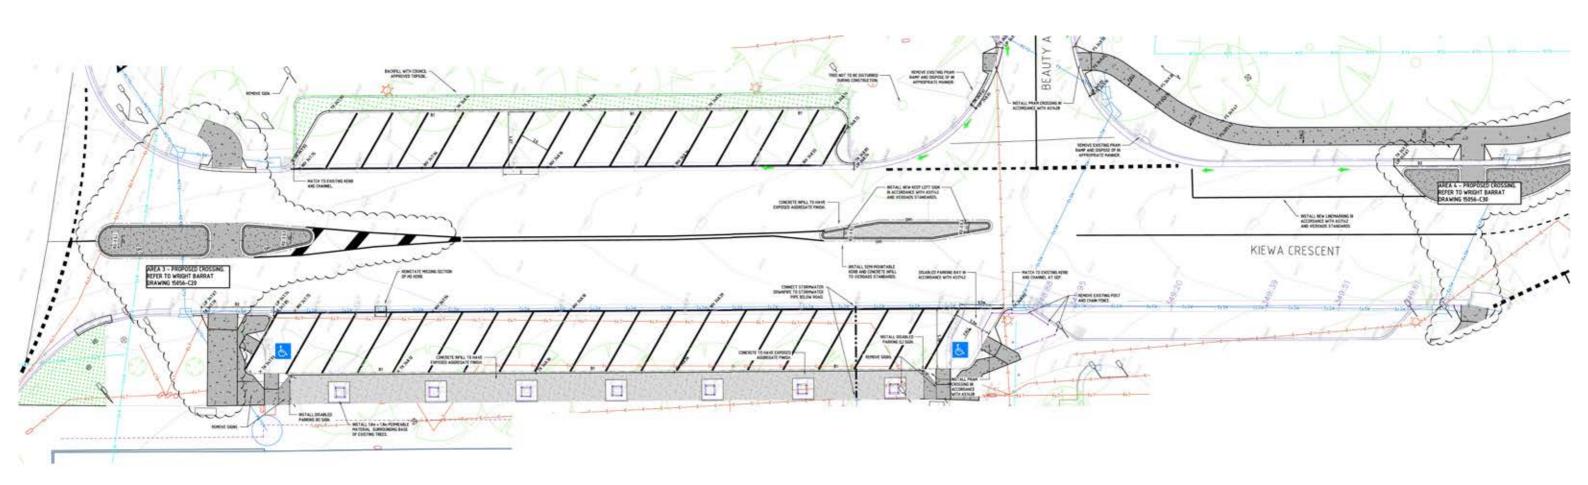

## MOUNT BEAUTY PROGRESSING PLACE PROJECT PROPOSED TOWN CENTRE KERB WORKS

20 November 2015

